

ENTERPRISE AI OPERATING MODEL · PROOF OF CONCEPT KICKOFF

Standing up your agent fabric

Build the substrate once. Prove it on your own software delivery.
Then every capability after it gets faster, cheaper and safer to ship —
measurably, from week three.

Build the fabric once, prove it on your own software delivery, and every capability after it gets faster, cheaper and safer.

SITUATION

Models are good enough. [CLIENT]'s teams can each build an agent, and several already have.

COMPLICATION

Nothing is shared between them. Every agent resolves identity, policy, telemetry and release — so cost per capability never falls and nothing reaches production.

RESOLUTION

Build the shared substrate once — registry, authority, one event spine, a paved road — and prove it on agentic software delivery, which is internal, reversible and measurable in three weeks.

THE FABRIC MOVES FOUR RATIOS — AND ONLY THESE FOUR

↓ Time-to-capability

Days from "we want this" to it running in production, governed.

↓ Cost-per-capability

Fully loaded cost of capability n . The compounding term.

↓ Risk-per-capability

Blast radius × exposure, evidenced rather than asserted.

↑ Reuse rate

Share of a new capability composed from ones that already exist.

THE ASK

One squad, twelve weeks

FROM YOU

~4 days/week across seven named people

NEW SPEND

No licences. Runs on what you already operate

FIRST PROOF

Week 3 — agents reviewing real pull requests


DECISION TODAY

Five, all listed on slide 24

The constraint is no longer model capability — it is that nothing is shared between one agent and the next.

Every team can build one agent. None can build the hundredth — because the hundredth needs a fabric, and building a fabric is nobody's job description. So each capability re-solves identity, policy, telemetry, release and evidence from scratch.

COST PER CAPABILITY — THE TWO TRAJECTORIES

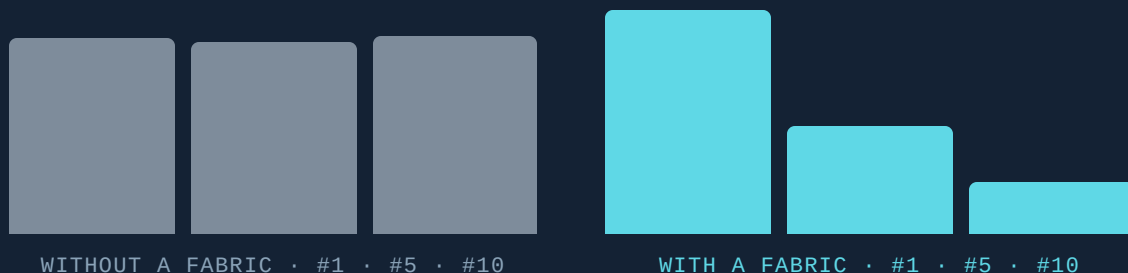

Illustrative shape. Capability #1 **pays for the fabric**; #10 carries only itself. Any business case that prices agent number one as a product decision will always say no — and will always be wrong.

WHAT THAT ARITHMETIC PRODUCES

Pilots that cannot graduate

Every promotion triggers a bespoke security, platform and data review, because there is no shared posture to inherit.

A parallel estate, quietly

The AI team stands up its own identity, secrets and logging — because waiting for the platform team was slower.

Answers nobody can evidence

"The model decided" offered to Risk, which no dashboard repairs after the fact.

None of these are model problems. All three are the same missing substrate, showing up in three different committees.

Four credible responses. Only one bends the cost curve without creating a second estate.

OPTION	WHAT IT IS	TIME TO FIRST VALUE	COST OF CAPABILITY #10	CONTROL POSTURE	WHY IT WINS OR LOSES
1 • Wait Let the market mature	Keep pilots in sandboxes; revisit in a year.	None	Unchanged — no learning curve started	Unchanged; shadow usage continues regardless	Losses. The fabric is where the learning compounds, and none of it is model-dependent. Waiting defers the learning, not the risk.
2 • Federated DIY Every squad builds its own	Teams ship agents independently with whatever they can reach.	FASTEST weeks	≈ same as #1 — nothing is shared	Divergent; ambient credentials by default	Losses at capability five. Genuinely the fastest to capability one — which is why most organisations are already here without deciding to be.
3 • Buy a platform Single vendor suite	Adopt one vendor's agent platform end to end.	Months — procurement first	Low, inside the suite	Strong but vendor-shaped	Losses on fit and exit. Assumes one vendor spans identity, data, platform and control. If a suite is already owned, we build around it rather than replace it.
4 • Platform-first, thin Recommended	Build only the shared contract — registry, authority, event spine, paved road — on incumbents.	WEEK 3 first proof	Materially lower — the fabric is already paid for	Uniform, evidenced, and yours	Wins. Twelve of fourteen components are reused. Two are new. Nothing is replaced, and every product underneath stays swappable.

What makes option 4 cheap is what makes it credible: it does not ask you to replace a single incumbent. Identity, CI/CD, observability, gateway, event bus and catalog all stay. We add a registry and a way to grant authority — and hand both over as your code.

The question we would like from this room: is there a fifth option we should have considered? If your organisation has a constraint that rules option 4 out, we would rather hear it in minute fifteen than discover it in week six.

Four things leave our hands and stay in yours — each moving a named ratio.

Twelve weeks, one squad, working software. Everything below is either running in your estate or checked into your repositories when we finish.

MOVES COST-PER-CAPABILITY

A working agent fabric

Capability registry, orchestration, delegation, identity and policy — deployed in your environment, on your platform.

You can: register a new capability and see it appear with an owner, a tier, health and an off switch.

MOVES TIME-TO-CAPABILITY

Agents doing real work

Agentic CI/CD: code review, test generation, dependency upgrades, release notes and deploy gating — on your repositories.

You can: open a pull request and get a substantive agent review before a human reads it.

MOVES REUSE RATE

The paved road

Templates, registration, policy inheritance, test harness, dashboards and runbooks — so the next squad does not need us.

You can: stand up a new capability in about a day, from documentation alone.

MOVES RISK-PER-CAPABILITY

The operating rhythm

Capability intake, tiering, release and evidence review — with the forums, owners and measures defined and running.

You can: answer "what are our agents doing, and is it working?" from one place, monthly.

Why delivery agents first? Internal, reversible, no customer exposure, and measurable inside three weeks — while exercising every plane of the fabric under real load. Business capabilities are path two, designed in week ten with everything we learned.

Four value drivers, one arithmetic each — so you can argue with the assumptions, not the conclusion.

THE VALUE TREE · EVERY TERM MEASURABLE FROM SYSTEMS YOU ALREADY RUN

① Throughput released

MEASURABLE WK 5

engineers in scope × share of time on assistable work × improvement rate

Assistable work is review, test authoring, dependency and migration toil, and release mechanics.
Baseline comes from your own SCM and CI data — not a survey.

② Capability cost avoided — the compounding term

GROWS

capabilities per year × (cost of capability #1 – cost of capability #n)

The only driver that grows with every capability you add. The other three are one-time step changes. After roughly two quarters this term dominates the page — which is the whole reason this is a platform decision.

③ Assurance effort released

MEASURABLE WK 9

control cycles per year × analyst-days per cycle × reduction rate

Evidence emitted continuously rather than assembled per review. The saving is analyst days, not software licences.

④ Integration avoided

MEASURABLE Q2

integrations per year × average build cost × avoidance rate

Shared capability contracts replace point-to-point work between teams and systems.

ILLUSTRATIVE ONLY — DRIVER ① WORKED THROUGH

Numbers below are **placeholders chosen to show the arithmetic**, not a forecast and not a benchmark. Every input is replaced with your measured data at gate 2.

Engineers in scope **200**

Share of time on assistable work **30%**

Improvement on that share **15%**

$$200 \times 30\% \times 15\% =$$

9.0

FTE-equivalent released per year

SENSITIVITY ON THE UNCERTAIN INPUT

10%
6.0

15%
9.0

20%
12.0

The POC's commercial job is to replace those three placeholders with measured values — and to tell you if the honest answer is lower than you hoped.

02

THE OFFER · INVESTMENT AND REUSE

Ten of fourteen components already exist in your estate — which is why twelve weeks is credible.

THE INVESTMENT · TWELVE WEEKS

Our delivery squad — 5 forward-deployed engineers	12 wks
Your team — seven named roles, part time	~4 d/wk
Infrastructure — your existing platform	no new spend
Incremental run cost — inference and control	[\$X]/mo
Licence commitments required to start	none
No procurement on the critical path. That single line removes what is usually the largest schedule risk in an enterprise programme.	
Nothing here is a platform purchase. The fabric is built from what you already run, plus two components handed over as your code.	

WHAT THE FABRIC NEEDS — AND WHO ALREADY HAS IT

COMPONENT	[CLIENT]	EFFORT	COMPONENT	[CLIENT]	EFFORT
Compute & orchestration	—	● REUSE	Messaging / event bus	—	● REUSE
Identity provider	—	● REUSE	Data platform & catalog	—	● REUSE
CI/CD pipelines	—	● REUSE	Approval tooling	—	● REUSE
Observability backend	—	● REUSE	Telemetry conventions	—	● EXTEND
API gateway / mesh	—	● REUSE	Policy & risk tiers	—	● EXTEND
Service catalog	—	● REUSE	Capability registry	—	NEW
Secrets management	—	● REUSE	Capability grants	—	NEW

Ten reuse, two extend, two new. If that ratio is wrong for [CLIENT], the twelve-week plan changes — and we would rather find out in the next five minutes than in week six.

One event spine returns three payoffs from a single investment — which is why it is funded once, not three times.

Most enterprises fund observability and eventing separately, out of different budgets, and build the same spine twice. Unify it once and agents become possible almost as a side effect.

THE SINGLE INVESTMENT

A unified event plane

One context propagated through every call. One bus. One schema for what happened, who asked, what was decided and what changed.

Built on what you run. Your existing bus, your existing observability backend. We add conventions, not infrastructure.

IN POC SCOPE

PAYOFF 01

Extensible observability

Every agent, service and decision on one correlated trace. New capabilities inherit instrumentation instead of adding a monitoring backlog item.

Who wins: platform, SRE, and every team that would otherwise be told to "add logging".

PAYOFF 02

Agent triggers

Work starts because something happened — a PR opened, a ticket raised, a threshold crossed — not because a human remembered to ask.

Who wins: AI practice and the business. **An agent that can only be called is a tool; one that can be triggered is a colleague.**

PAYOFF 03

Evidence as exhaust

The record auditors want is produced by the running system, continuously, rather than assembled by analysts before a review.

Who wins: governance, risk and audit — see the maturity path on slide 18.

The honest trade-off: one spine means one thing to get right. It needs schema discipline, back-pressure handling and an owner. We would rather you run one spine well than three badly — but it is a real commitment, and the platform team should hear that from us rather than discover it in month four.

THE PATTERN: FUND THE SUBSTRATE ONCE, COLLECT THE PAYOFFS MANY TIMES

Capability sandboxing is why you can let agents act, not just read.

Most enterprises keep agents read-only because the only way to let one act has been to hand it a credential — and a handed-over credential cannot be bounded afterwards. This removes that trade.

● WITHOUT IT

The agent holds a credential

It can reach anything that credential can reach — including things nobody thought about when it was issued.

Blast radius is whatever the credential allows, so the safe answer is always **read-only**.

A prompt-injected or simply mistaken agent has the same reach as a correct one.

Every new action needs a fresh review, because there is no boundary to reason about — only intentions.

The honest trade-off: the WASI toolchain is younger than containers, and not every workload compiles cleanly to it. We use it where the boundary earns its keep — agent tool execution — and ordinary containers everywhere else. This is a pattern, not a migration.

WITH WASI CAPABILITY SANDBOXING

The agent holds only declared doors

It runs inside a sandbox where **only the capabilities it declared exist at all** — no ambient filesystem, network or credential.

Blast radius is the declaration, which is readable, reviewable and diffable in a pull request.

An injected or mistaken agent still cannot reach what was never wired to it.

New actions are a **change to a manifest**, reviewed like code — not a new security engagement.

Net effect: the organisation can say yes to writes, with a bounded answer

What this unlocks commercially: tier-1 and tier-2 write actions ship on the paved road with a manifest review, instead of queueing for a bespoke security assessment. That queue is usually the single largest source of delay between a working agent and a useful one.

Shared vocabulary is what turns compliance and integration from projects into properties.

Two of the most expensive recurring costs in a large enterprise have the same root cause: nothing agrees on what things are called. The operating model fixes that incrementally, as a by-product of registering capabilities.

PAYOFF 01

Agile compliance

When a capability declares what it does, to which entities, under which classification — and the event plane records every use — a control question becomes a **query** rather than a project.

- Controls are evidenced continuously, not reconstructed quarterly
- A new regulation maps to existing declarations instead of a discovery exercise
- Risk reviews shift from interviewing teams to reading the record

Measured as: analyst-days per control cycle, and time to answer a novel

PAYOFF 02

Cross-functional integration

When capabilities are described in business terms rather than endpoints, teams compose them without meeting first. The vocabulary becomes the integration layer.

- An agent asks for a *capability*, not a system — so ownership can change underneath
- Point-to-point integrations stop multiplying with every new consumer
- Teams discover existing capability instead of rebuilding it in a different silo

Sequencing, stated plainly, because this is where these programmes die: we are not starting an ontology programme. In the twelve weeks we do **provenance and grounded retrieval only** — every answer carries its source, timestamp and owner. Vocabulary grows one domain at a time, where it earns its keep, and every capability registered on the paved road contributes to it at no extra cost. If **[CLIENT]** has an ontology or data-mesh programme in flight, this feeds it rather than competing with it.

The first agents build your software. That is deliberate.

Agentic CI/CD and agentic code review are the POC default — internal, reversible, measurable in three weeks, and they exercise every plane of the fabric under genuine load.

1

Trigger

A pull request opens. The event plane starts the work — nobody has to remember to ask.

2

Agentic review

Correctness, tests, security patterns and house conventions — with the reasoning attached to the diff.

3

Test generation

Missing cases proposed as code, in your framework, for a human to accept or reject.

4

Policy gate

Risk tier checked, capability manifests diffed, evidence recorded — automatically.

5

Staged release

Deploy behind the same grants and off switch as any other governed action.

6

Learn

Accept and reject rates feed back. The reviewer improves against your codebase, not a benchmark.

REASON 01

Internal

No customer exposure, no production data, no regulatory surface. Nobody needs to approve an experiment on their own repositories.

REASON 02

Reversible

Every action is a commit, a comment or a pipeline run. The undo procedure already exists and your engineers already know it.

REASON 03

Measurable in three weeks

Review latency, rework rate and change lead time — against a baseline your tooling already holds.

REASON 04

It exercises everything

Identity, policy, grants, triggers, evidence and sandboxing all get used under real load. **The fabric is built using the fabric** — so we feel any friction first, in week four.

The fabric is working when nobody notices it — it just shows up as an ordinary Tuesday.

Priya is a senior engineer on the payments squad, four months in. Nothing below is speculative — each moment is a capability the fabric supports at day 90.

08:55

She opens a pull request

Within ninety seconds an agent has reviewed it — correctness, missing test cases, a deprecated internal API she did not know about — with reasoning attached to each line.

TRIGGER · AGENTIC REVIEW

09:40

She disagrees with one comment

She replies, explains why, and merges. The disagreement is recorded and becomes signal — the reviewer gets better against *this* codebase.

HUMAN STAYS IN CHARGE

11:20

She needs customer data for a fix

She asks in the portal. The capability exists, her tier permits it, and she gets a scoped, time-boxed answer with sources cited — no ticket, no waiting.

REGISTRY · GRANTS · RETRIEVAL

14:00

A dependency CVE lands

An agent has already opened the upgrade PR across eleven repositories, run the tests and flagged the two that need a human. She reviews those two.

EVENT TRIGGER · FAN-OUT

16:30

She ships

The policy gate checks the tier and the capability manifest, staged rollout begins, and the evidence record is complete before she closes her laptop.

GOVERNED RELEASE

Now notice who else had a good Tuesday, without attending a single meeting about AI. **Platform** saw every agent action on the same dashboards as everything else. **Risk** had eleven CVE remediations evidenced automatically. **The product owner** got a day of Priya's time back. **Data governance** can show exactly which customer records were read, by whom, under which purpose.

Seven roles and four days a week between them — and nobody has to become an AI specialist.

ROLE	WHERE YOU WORK ON THE CANVAS	WHAT YOU OWN	WHAT WE NEED FROM YOU	TIME
Product & business owner	Experience · the four ratios	Naming the capability and the outcome it serves; accepting or rejecting what ships	One named person who can say yes without convening others	2 h/wk
AI practice lead	Agent Fabric	Agent design, the capability backlog, and how quality is evaluated	The capability inventory, and your evaluation approach today	1 d/wk
Architecture	All planes — the coherence owner	That the planes stay separable and the contracts hold as things are added	Current-state view and any standing architectural decisions we must respect	0.5 d/wk
Platform & DevOps	Platform · Event Plane	The paved road, the event spine, and running all of it after week 12	A non-prod namespace in week 1, and authority over the deployment template	1 d/wk
Data engineering	Knowledge · Systems	Capability contracts on data products; freshness and provenance	Catalog read access and the freshness SLA of the sources we ground on	0.5 d/wk
Governance & risk	Control · Knowledge	Risk tiers, what evidence must show, and who may assign a tier	Three tiers roughly defined, plus the one data class that is out of bounds	0.5 d/wk
Our FDE team	Across every plane, then out	Building it, proving it, documenting it and handing it over	Honest correction when we get your environment wrong	5 people

If a role cannot be named today, we need a date. Unnamed roles are the single most reliable predictor of a slipped milestone — ahead of any technical risk on the register.

Only five activities are genuinely joint — everything else has a single, named owner.

■ **We lead** — our team drives, you review ■ **You lead** — only your organisation can do this ■ **Genuinely joint** — neither of us can do it alone

ACTIVITY	WE LEAD	YOU LEAD	JOINT	NOTE
Choosing the first squad and repositories		■		You know which team wants this most. That matters more than which codebase is tidiest.
Defining risk tiers and who assigns them			■	We bring the shape; only you can set the thresholds.
Environment, identity and repository access		■		The most common cause of slipped milestones. Week 1.
Building the capability registry and grants	■			The two genuinely new components. Handed over as your code.
Event plane conventions on your existing bus			■	Our schema, your operational reality.
Agentic review, test generation, deploy gating	■			Tuned against your codebase and your house conventions.
Deciding what "good enough to merge" means		■		Your engineering standards, not ours. We encode them.
Golden-path templates and documentation	■			Written for your platform, in your conventions.
Value baselines and how we report them			■	Your data, our model. Agreed in week 1, fixed in week 2.
Capability backlog beyond the first workload			■	We facilitate; the business decides.
Evidence review and the control crosswalk			■	Your assessors' frameworks, our architecture evidence.
Running the fabric after week 12		■		Proven in week 11 — a second squad onboards with us out of the room.

Seven recurring decisions, each with one decider, one forum and one cadence.

DECISION	DECIDED BY	CONSULTED	FORUM	CADENCE	ESCALATES TO
Which capability is built next	Product & business owner	AI practice · architecture	Capability intake	Weekly	Sponsor
Risk tier assigned to a capability	Governance lead	Capability owner · security	Intake (T1/T2) · risk forum (T3)	Weekly / on demand	CISO delegate
Whether a capability may go live	Capability owner (T1/T2) Named approver (T3)	Platform · security	Release gate — automated checks	Continuous	Governance lead
Whether the manifest change is acceptable	Reviewing engineer	Security, if the tier changes	The pull request itself	Per change	Governance lead
Whether to trip a circuit breaker	The on-call engineer	Nobody — act first	None. There is no forum.	Immediate	Explain afterwards
Whether a policy or tier definition changes	Governance lead	Architecture · AI practice · platform	Policy review	Monthly	Sponsor
Whether the next roadmap move happens	Executive sponsor	All seven roles	Quarterly review	Quarterly	—

The breaker row is the one to notice. No forum, no consultation, act first. If stopping something requires a meeting, you do not have an off switch — you have a suggestion.

Reuse a forum wherever one exists. If **[CLIENT]** already has an architecture council, a change board or a risk forum that fits a row, we use it. Creating governance is a last resort, not a deliverable.

Every function gains something specific — and gives up something small enough to name.

PLATFORM & DEVOPS

YOU GAIN

Every agent lands on **your** platform, in **your** pipelines, on **your** dashboards — instead of a shadow stack in a different budget line. One off switch per capability. An event spine you would have wanted anyway.

YOU GIVE UP

A registration step enters the service lifecycle. Deployment templates gain a sidecar and a telemetry contract by default.

WE NEED

Non-prod namespace, week 1. One engineer at 1 d/wk with real authority over the template. An honest p99 latency budget.

AI PRACTICE

YOU GAIN

A capability that fits an approved tier **inherits its policy** instead of negotiating one. Promotion becomes a checklist, not a committee. Delegation becomes expressible. Models, prompts, frameworks and eval stack stay entirely yours.

YOU GIVE UP

The long-lived credential that "just makes the demo work". Capabilities need a declared scope before first use — about a day, once, each.

WE NEED

The capability inventory for the first workload. One practitioner at 1 d/wk.

DATA ENGINEERING

YOU GAIN

No new pipelines in twelve weeks — curated existing sources only. Retrieval is never asked to be a security boundary. Data products gain a capability contract, reusing your catalog. Consumers finally become visible.

YOU GIVE UP

Sources used for grounding must carry provenance — source, timestamp, owner. That is a standard, not a project.

WE NEED

Catalog read access, week 1. Freshness SLAs for the sources we ground on. 0.5 d/wk.

GOVERNANCE & RISK

YOU GAIN

Classification becomes enforceable at access time, not asserted in a catalog. Purpose becomes expressible and checkable. Evidence is continuous — you stop assembling it and start querying it.

YOU GIVE UP

Tiers must be defined and owned rather than decided case by case. That is the trade that makes self-service possible.

WE NEED

Three tiers roughly defined, week 1. Who assigns them. The one out-of-bounds data class. 0.5 d/wk.

If **[CLIENT]** has an ontology, data-mesh or catalog programme in flight: we feed it rather than compete with it. Everything the fabric emits — capability semantics, provenance, ownership, purpose — is structured input that programme can consume. We are neither waiting for it nor duplicating it.

The twelve weeks delivers level one across all five segments — everything right of that is a later choice.

	YOU ARE HERE	LEVEL 1 · FOUNDATION — WEEKS 1-12	LEVEL 2 · SCALE — QUARTERS 2-3	LEVEL 3 · COMPOUNDING — QUARTER 4+
Agent fabric Registry, orchestration, delegation	mark →	POC Capabilities registered with owner, tier and health. One squad building on templates.	Self-service onboarding across squads. Delegation between agents. A backlog owned by the business.	TARGET Portfolio management — capabilities retired, versioned and reused as deliberately as microservices.
Event plane Observability and triggers	mark →	POC One correlated context across agents and services. Events trigger the delivery agents.	Business events trigger business capabilities. Evidence stream feeds risk reporting directly.	TARGET Governed autonomous operations — the system reacts within policy, humans supervise by exception.
Knowledge Meaning, grounding, memory	mark →	POC Provenance and grounded retrieval. Every answer carries source, timestamp and owner.	Shared vocabulary for one or two domains. Entity resolution where it pays.	TARGET Federated ontology across domains — compliance and integration become properties, not projects.
Safe execution Tiers, sandboxing, authority	mark →	POC Three risk tiers. Capability manifests reviewed as code. Sandboxed writes on tier 1 and 2.	Tier assignment self-served against clear criteria. Security review becomes exception handling.	TARGET Policy as code at scale — new regulation lands as a policy change, not a programme.
Agentic delivery How software gets built	mark →	POC Review, test generation and deploy gating on one squad's repositories.	All squads. Cross-repository maintenance — dependency, CVE and migration work by fan-out.	TARGET Agents hold routine maintenance entirely; engineers spend their time on design and judgement.

Two things we would like from this room before we move on: mark where you are today in column one, and tell us which of the five matters most to **[CLIENT]**. Expect disagreement — governance, platform and AI practice will each pick a different segment, and that prioritisation conversation is far cheaper to have now than in month three.

Six moves, each with a reason, its payoffs and an honest cost — because a roadmap without trade-offs is a wish list.

NOW · IN THE 12 WEEKS

Unify the event plane

Observability and eventing are the same spine funded from two budgets. Build it once.

- Extensible observability across every agent and service
- Agent triggers — work starts from events, not reminders
- Evidence produced as exhaust

COSTS YOU

Schema discipline, back-pressure handling and a named owner. One spine means one thing to get right.

NOW · IN THE 12 WEEKS

Sandbox agent execution

The only reason agents stay read-only is that a handed-over credential cannot be bounded afterwards.

- Write actions become approvable at tier 1 and 2
- Manifest review replaces the bespoke security queue
- Blast radius becomes a diff, not a discussion

COSTS YOU

A younger toolchain than containers, and not every workload compiles to it. Use it where the boundary earns its keep.

QUARTER 2 · CHOICE

Agentic delivery everywhere

The first squad's throughput gain is the proof; the portfolio gain needs every squad on it.

- Cycle-time improvement across the whole engineering org
- Consistency — house conventions applied uniformly
- Cross-repo maintenance by fan-out, not by ticket

COSTS YOU

Review fatigue is real. Needs quality gates and a way for engineers to reject and be heard, or trust erodes fast.

QUARTER 2-3 · CHOICE

Shared vocabulary for one domain

Compliance effort and integration cost have the same root cause: nothing agrees on what things are called.

- Agile compliance — controls evidenced, not reconstructed
- Cross-functional integration without a meeting first
- Capability reuse rather than silo rebuild

COSTS YOU

Needs a domain owner with authority, and shows value slowly. Start with one domain — never enterprise-wide.

QUARTER 3 · CHOICE

Policy as code at scale

Tier assignment done by humans is a queue; done by criteria it is a checklist.

- Squads self-serve tiers against clear criteria
- Security review becomes exception handling
- New regulation lands as a policy change, not a programme

COSTS YOU

Policy authoring becomes a real skill someone must hold. Done badly, it is worse than the queue it replaced.

QUARTER 4+ · WHERE IT GOES

Governed autonomous operations

Once evidence is trustworthy, the system can respond within policy and humans supervise by exception.

- Remediation and scaling handled inside guardrails
- Operational cost decoupled from portfolio growth
- Engineers on design and judgement, not toil

COSTS YOU

Requires evidence maturity you will not have for a while. **On this page because it is where this goes — not because we think you should do it next year.**

The order is not a preference — each step removes the constraint on the next.

1

Name things

Identity and the capability registry. Every capability gets an owner, a tier, a schema and a version.

Removes the constraint: you cannot grant authority to something you cannot name, and you cannot measure a portfolio you cannot list.

2

Make it visible

The event plane. One correlated context across agents and services, carrying both telemetry and triggers.

Removes the constraint: improvement cannot be claimed without a baseline carrier, and triggers cannot exist without the spine.

3

Make writes safe

Capability grants and sandboxed execution. Authority that expires, inside a boundary that is declared.

Removes the constraint: writes need both an expiring authority *and* a bounded runtime — and both need step one to know who is asking.

4

Pave the road

Templates, policy inheritance, tests, dashboards and documentation, encoding what steps one to three proved.

Removes the constraint: the next squad no longer needs us — which is the only definition of success that survives our departure.

WHAT BREAKS IF YOU REORDER — THE REASON THIS IS NOT NEGOTIABLE ON PREFERENCE ALONE


TEMPTING REORDER	WHY IT IS TEMPTING	WHAT ACTUALLY HAPPENS
Paved road first	It is the visible deliverable, and platform teams ask for it.	Templates can only encode conventions that already exist. Build the road first and you template guesses — then every squad inherits those guesses, and unpicking them costs more than the road saved.
Sandboxing first	It looks like the safety-critical piece, so it feels responsible.	A sandbox with nothing to grant to is a container with extra steps. Isolation without an authority model bounds the runtime but not the permission — which is the part that actually goes wrong.
Event plane last	It reads as observability, which sounds like a phase-two concern.	You lose the baseline. Improvement claimed without a pre-measured baseline is unfalsifiable, and gate 2 becomes a matter of opinion rather than evidence.
Business capability first	It is the one the board asked about.	You learn the fabric and an unfamiliar business domain simultaneously, with customer exposure. That is how twelve weeks becomes twenty — and the failure gets attributed to the architecture rather than the sequencing.

The question worth asking us: is there a constraint in **[CLIENT]** 's environment that forces a different order? A long identity-provider change window, for example, sometimes genuinely requires splitting step one. We would rather redesign the sequence in week zero than discover the constraint in week four.

EGISES

ENTERPRISE AI OPERATING MODEL · POC KICKOFF

Agents review real pull requests in week three; everything after that is widening and hardening.

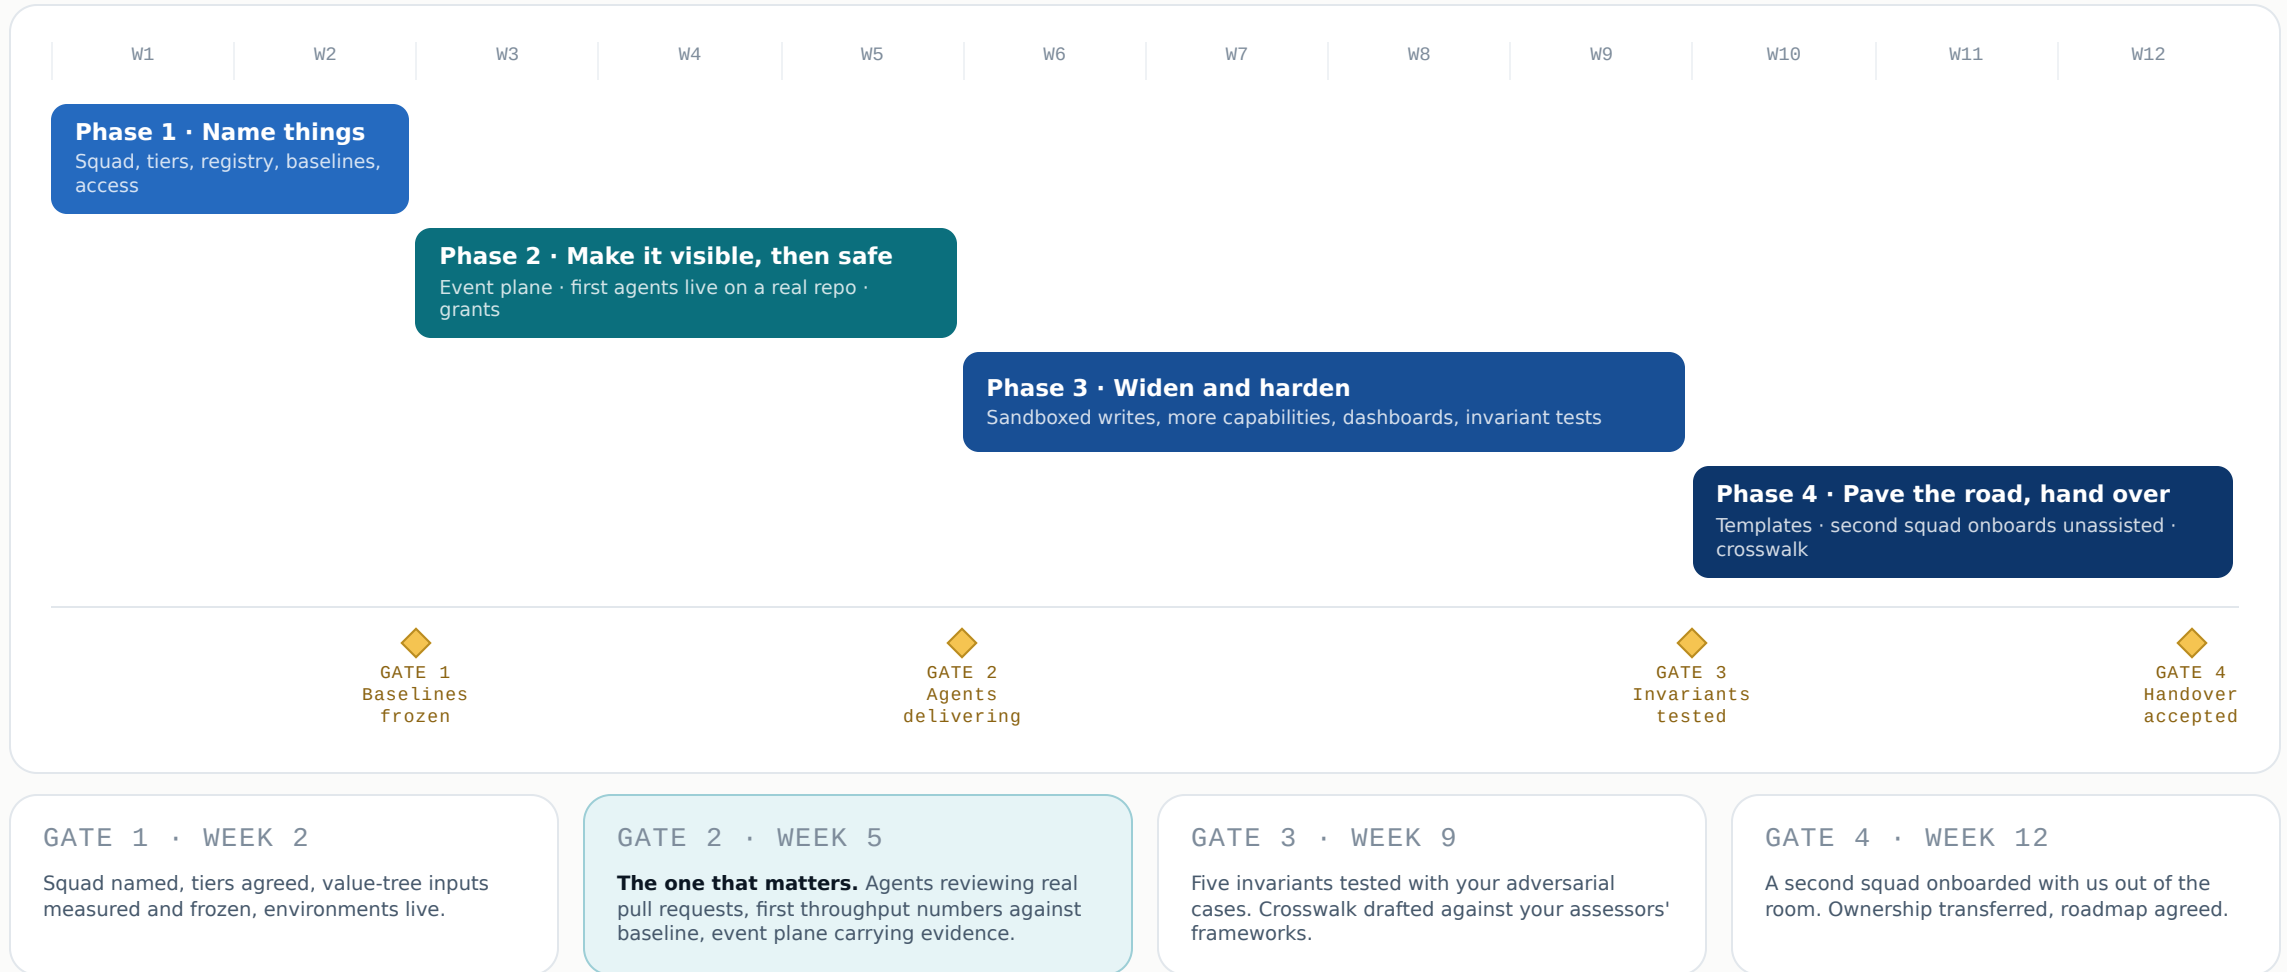

Every item below is a noun you can open, run or read.

No workstreams, no enablement, no alignment. If it cannot be pointed at, it is not on this slide.

DAY 1 · END OF WEEK 1

The **first squad** named, with a product owner

Three **risk tiers** defined, with an assignment owner

Value-tree inputs **measured** — review latency, rework, lead time

Seven **named people** and a fixed weekly slot

A **decision log** with entries in it

Environment and repository access **requested, with dates**

DAY 30 · END OF WEEK 4

Agents reviewing real pull requests on your repositories

A **capability registry** with owners, tiers and health

The **event plane** carrying one correlated context

First **throughput numbers** against your own baseline

Sandboxed execution running **tier-1 write actions**

A frank week-5 gate paper, **including what is not working**

DAY 90 · END OF WEEK 12

A **paved road**: templates, registration, policy inheritance, tests, dashboards, off switches

Agentic delivery across **review, tests, dependencies, release notes and deploy gating**

A **capability portal** showing what exists, who owns it and whether it is healthy

A **control crosswalk** with sample evidence, reviewed by your assessors

A **second squad** that onboarded from documentation alone

A **measured value report** against the value tree, and a next-quarter roadmap

All of it yours whether or not you continue with us.

Three dependencies, and the dates that decide whether gate 2 holds.

ACCESS

Repositories for the first squad — read and PR	W1
CI/CD pipeline access for that squad	W1
Non-production namespace and deploy path	W1
Identity provider tenant — non-prod, with admin	W1
Observability backend — write and query	W2
Service catalog / CMDB — read	W2

The honest question: how long do these genuinely take here — not the SLA, the reality? If it is six weeks, it starts before the contract is signed.

DECISIONS

First squad and product owner confirmed	Today
Agentic delivery confirmed as first workload	Today
Three risk tiers, and who assigns them	W1
Incumbent platforms confirmed	W1
Data class that is out of bounds	W1
Value-tree inputs measured and frozen	W2
What "good enough to merge" means here	W2

PEOPLE & RHYTHM

Seven named roles — slide 14	Today
Weekly 45-minute working session, fixed slot	W1
Gate reviews — 60 min, sponsor present	W2/5/9/12
Shared channel and one written decision log	W1
Your change-freeze calendar	W1

One question we need answered today: what falls inside this twelve-week window — freezes, audits, quarter close, holidays? Those have derailed more of these than any technical risk.

Five decisions, and we start Monday.

Taken one at a time. Where we cannot decide today, we need a name and a date — an undecided item with no owner becomes a slipped gate in week three.

DECISION	WHAT WE NEED TO HEAR	OWNER	STATUS
1 The first squad	A named team, their repositories, and a product owner who can say yes without convening others. Pick the team that <i>wants</i> this, not the tidiest codebase.	—	OPEN
2 Agentic delivery as the first workload	Confirmation that we start with code review, test generation and deploy gating — and that business capabilities are path two, designed in week ten.	—	OPEN
3 The incumbent platforms	Which identity provider, observability backend, gateway and event bus we build on rather than replace.	—	OPEN
4 The seven roles and the rhythm	Names against slide 14 — or a date by which we will have them — and a fixed weekly slot starting this week.	—	OPEN
5 The value-tree inputs	Which of the four drivers we report against, and who owns measuring the baseline. We measure what you will actually be asked about.	—	OPEN

WITHIN 24 HOURS

Written confirmation of every decision above, access requests raised with dates, and the first weekly session in calendars. Nothing agreed in this room survives on memory alone.

WITHIN 5 WORKING DAYS


The week-1 working session — half a day, the seven named people, value-tree inputs measured, and the component map on slide 8 completed properly rather than live-edited.



**Build the fabric once.
Let every team use it.
Start with the software
you already know how to judge.**

The canvas in architectural form.

Responsibilities are fixed; product selections are contextual. This is slide 4 for an audience that reads architecture faster than infographics.

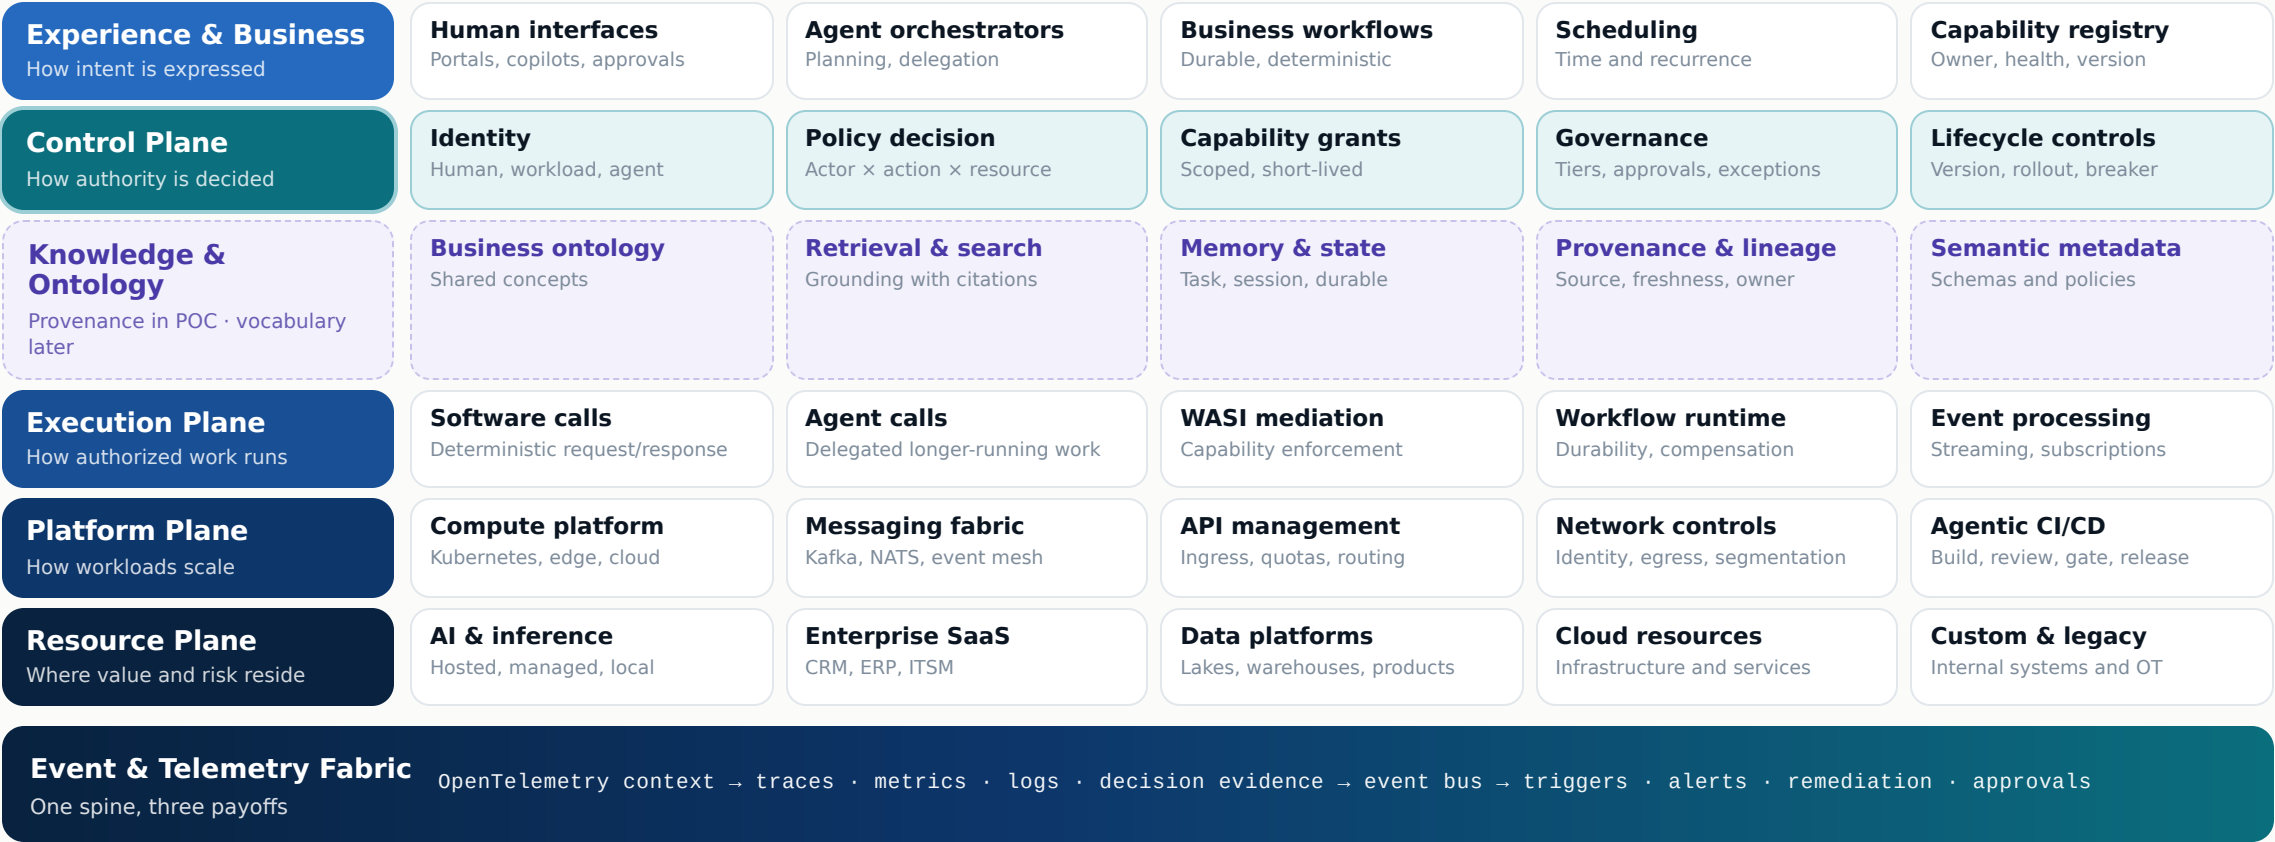

Five responsibilities, four of which you already have.

Standardize these; keep every product underneath them replaceable. The one that is usually genuinely new is capability grants.

RESPONSIBILITY	ANSWERS	IN ESTATE?
Identity Human, workload, agent	Who or what is acting, and on whose behalf?	 REUSE
Policy decision Actor × action × resource × context	May this actor perform this action, right now?	 EXTEND
Capability grants Scoped, short-lived, attenuable	How is that decision carried to the thing enforcing it?	 NEW
Governance Tiers, approvals, exceptions	Who decided this action class was acceptable, and when?	 REUSE
Lifecycle controls Version, rollout, breaker	How do we stop it — in seconds, without a deploy?	 EXTEND

A GRANT IS NOT A ROLE

A role describes what an actor **is**, and persists. A grant describes what an actor **may do** — bound to audience, action, scope and expiry — and is designed to die.

- **Audience-bound** — usable only at the intended resource
- **Attenuable** — a holder can narrow it, never widen it
- **Short-lived** — expiry is the default revocation mechanism
- **Verifiable offline** — routine work needs no round trip

The design tension, resolved in week 4: offline verification gives you latency; online decisions give you instant revocation. High-risk actions get the round trip; routine actions get local verification with a short TTL. Where **[CLIENT]** draws that line is a governance decision, not an engineering one.

Eight steps, and the record they produce.

Implementation varies by risk tier; the logical sequence does not. Steps 4 and 5 are the crux — the decision, and the conveyance of that decision.



```
trace_id 4f2a...c81b  on_behalf_of user: [EMPLOYEE]  actor agent:pr-reviewer/v3.1  workload spiffe:///.../review
capability repo.pr.comment  decision permit  policy tier1-delivery@v11  grant aud=scm scope=pr:comment ttl=90s
enforced_at wasi-sandbox/v2.4  manifest net:scm-api · fs:none · env:none  side_effects 1 comment · reversible  outcome ok · 214ms
```

This record is the assurance deliverable. If an auditor can read it without a human narrating what the agent "was trying to do", every claim on the crosswalk becomes checkable rather than asserted.

Five invariants, each with a test we run in week nine.

Principles are cheap; principles with a stated test are an engineering commitment. Your security and SRE teams are invited to design the adversarial cases.

INVARIANT	WHAT IT MEANS	HOW YOU TEST IT — AND WHAT A PASS LOOKS LIKE
1 Authority is explicit	No ambient access. Every action attributable to an identity and a decision.	Pick any action from the last 24 hours at random. Produce actor, human principal, decision, grant and expiry in under 60 seconds , without asking an engineer.
2 Delegation only narrows	Sub-agents receive subsets of authority — never amplification.	Have a sub-agent attempt an action its parent could not perform. It must fail closed , and the denial must appear in evidence with the attenuation reason.
3 Execution is bounded	The capability manifest is the blast radius, and it is reviewable.	Attempt an action outside the declared manifest — a network egress or file read never wired in. It must be impossible, not merely refused .
4 Everything is observable	Policy, routing, runtime and business outcome share one correlated context.	One trace identifier joins intent → decision → grant → runtime → backend → outcome across at least three systems , with no manual stitching.
5 Technology is replaceable	Interfaces and responsibilities standardized; products chosen by context.	Swap the policy engine — or the gateway — behind the same contract. Zero service code changes , and evidence continuity preserved across the swap.

Open invitation: your security and SRE teams design the adversarial cases for tests 2, 3 and 5. We would rather be broken by you in week nine than by an incident in month nine. If you want a sixth invariant, we will add it.

Isolation cost matched to consequence, not applied uniformly.

Tiers are set with [CLIENT] in week one. These are the shapes we start the conversation from — not a standard we impose.

TIER	CHARACTERISTIC	EXAMPLES IN DELIVERY	ISOLATION	APPROVAL PATH
Tier 1 SELF-SERVICE	Reversible, internal, no personal or regulated data, bounded output	PR comments, test generation, release notes, documentation	WASI sandbox, declared manifest, short-lived grant	Manifest reviewed in the pull request. No separate approval.
Tier 2 OWNER APPROVES	Reversible writes to systems of record, or reads of classified data	Dependency upgrades, branch creation, ticket updates, grounded answers on customer data	WASI sandbox plus online policy decision for the write	Capability owner approves the tier assignment once, not each use.
Tier 3 GOVERNED	Irreversible, customer-facing, financially material, or regulated action	Production deploys to regulated systems, anything touching money or customers directly	Sandbox, online decision, human in the loop, staged rollout	Named human approval per action or per batch, recorded as evidence.

WHY NOT ISOLATE EVERYTHING AT TIER 3

Uniform maximum isolation is either unaffordable everywhere or quietly bypassed where it hurts. Tiering is what keeps the strong controls credible in the places they actually matter.

WHERE THE POC SITS

Agentic delivery is almost entirely **tier 1**, with a small tier-2 surface for dependency upgrades and branch writes. That is precisely why it is the right first workload — real writes, bounded consequence.

Evidence in a shape your existing frameworks already accept.

Which of these bind [CLIENT]? Mark them and we scope the week-9 crosswalk accordingly.

ARCHITECTURE EVIDENCE	NIST AI RMF	ZERO TRUST · SP 800-207	ISO/IEC 42001	SOC 2 · EU AI ACT
Attribution record Actor, human principal, decision	MAP · MANAGE	Policy decision point logging	Operational planning & control	CC6 logical access · Art. 12 record-keeping
Grant scope & expiry Audience, action, TTL, attenuation	GOVERN · MANAGE	Per-session least privilege	Resource & access control	CC6 logical access
Capability manifest Declared, reviewed, diffed	MAP · MEASURE	Asset & resource classification	AI system impact assessment	CC6 · Art. 9 risk management
Denial evidence Refused attempts and reasons	MEASURE	Continuous verification	Performance evaluation	CC7 system operations
Correlated invocation trace Intent → outcome, ≥3 systems	MEASURE · MANAGE	Monitoring & diagnostics	Monitoring, measurement, analysis	CC7 · Art. 12 logging
Circuit breaker & revocation Time-to-stop, measured	MANAGE	Dynamic policy enforcement	Incident & nonconformity	CC7 · Art. 14 human oversight

Stated plainly: a twelve-week proof of concept produces *evidence samples* mapped to these controls. It does not produce a certified control, an audit pass or a compliance assertion. What it produces is a defensible case that the evidence a full implementation generates is the evidence your assessors need.

What could go wrong, and when we would tell you to stop.

Almost every mitigation below is early detection rather than clever engineering. We are happy to write the stop conditions into the statement of work.

RISKS

	RISK	MITIGATION	OWNER
1	Access slips beyond week 2	Requests raised day 1, tracked in the decision log, escalated weekly. Gate 1 is not complete without it.	Sponsor
2	The first squad does not want it	Pick the team that asked, not the one assigned. A named fallback squad costs nothing before week 3.	Joint
3	Agent review quality is poor on this codebase	Measured from week 3 with accept/reject rates. Tuning is expected; if it is still poor at gate 2, we say so.	Us
4	Review fatigue erodes trust	Signal-to-noise tracked explicitly. Agents stay quiet by default and earn the right to comment.	Joint
5	A change freeze falls in the window	Freeze calendar reviewed week 1; phases shifted around it rather than compressed into it.	Platform
6	Key people pulled to an incident	Named deputy per role. A written decision log means context survives an absence.	Sponsor
7	Scope widens after a good demo	Every addition displaces something of equal size, recorded in the gate note with both names on it.	Joint

STOP CONDITIONS

- 1 • **No measurable throughput signal by gate 2.** If agentic delivery cannot move review latency or rework on a willing squad in five weeks, the workload choice is wrong.

2 • **Enforcement cost is unaffordable.** If policy and sandboxing add more than the agreed budget to the hot path and cannot be tiered or cached down, the model does not fit this estate.

3 • **Evidence cannot be correlated.** If a trace cannot be joined across three systems without manual stitching, every downstream assurance claim rests on sand.

4 • **The squad will not adopt without us in the room.** This is the failure mode that kills programmes six months after the consultants leave.

5 • **[YOUR FIFTH]** — proposed by the client. We will write it in.

How a stop actually works: a written finding within 48 hours, joint review inside a week, then one of three outcomes — remediate with a named change and a new date, re-scope, or stop. **You keep the artefacts in all three cases.**

Choose technology by responsibility, not by category.

We hold no commercial relationship with anything named here. If your incumbent is missing, that is a gap in our knowledge rather than a judgement on your choice.

CONTROL & IDENTITY

RESPONSIBILITY	REPRESENTATIVE OPTIONS	WORKING POSTURE
Enterprise identity	Entra, Okta, Keycloak, cloud IAM	REUSE FIRST No parallel identity estate for agents.
Workload identity	SPIFFE/SPIRE, mesh identity, cloud workload identity	ADD WHERE NEEDED Where service accounts are too blunt.
Policy decision	OPA/Rego, Cedar, OpenFGA, IAM-native ABAC	SMALL VOCABULARY Business concepts, not engine syntax.
Authority conveyance	Signed tokens, caveated credentials, mTLS-bound grants	HYBRID Local for routine; online for high risk.

EXECUTION, PLATFORM & EVIDENCE

RESPONSIBILITY	REPRESENTATIVE OPTIONS	WORKING POSTURE
Agent isolation	WASI runtimes, sandboxed containers, microVMs	RISK TIERED Match isolation cost to consequence.
Event fabric	Kafka, NATS, Pulsar, cloud event services	REUSE FIRST One spine; conventions, not new infrastructure.
Telemetry contract	OpenTelemetry APIs, SDKs, collectors, conventions	STANDARDIZE One invocation context, end to end.
Observability backend	Grafana, Datadog, Splunk, Elastic, cloud APM, SIEM	REUSE FIRST No separate estate solely for agents.

Selection criteria applied throughout: explainability of decisions · deterministic evaluation · attenuation and audience binding · offline verifiability · blast-radius containment · operational maturity in *your* hands, not ours.

Six terms this deck uses precisely.

Each is commonly used loosely. Where a definitional argument starts, it usually ends here.

Agent fabric

The shared substrate that makes the second, tenth and hundredth agent cheap to build and safe to run: registry, orchestration, delegation, identity, policy, event spine and paved road. Distinct from any individual agent.

Capability

A named, owned, tiered thing an agent or service can do, described in business terms rather than as an endpoint. The unit of registration, of policy and of reuse.

Capability grant

A short-lived, audience-bound, attenuable credential conveying a specific authorization decision to the point that enforces it. Distinct from a role, which describes what an actor is and persists indefinitely.

Capability manifest

The declaration of exactly which doors an agent's sandbox opens — network, filesystem, credentials. Reviewed and diffed like code; it *is* the blast radius.

Event plane

One spine carrying both telemetry and triggers, so observability, agent activation and evidence come from a single investment rather than three.

Paved road

The supported, templated, instrumented route by which a team registers and operates a capability. Its quality is measured by adoption without its authors present.

Week-0 intake — the fields this deck is parameterised on.

Every bracketed field resolves from this sheet. Press **E** on any slide to highlight them.

ENGAGEMENT	FIRST SQUAD & MEASURES	ESTATE & PEOPLE
[CLIENT] —	Squad name and product owner —	Identity provider —
[DATE] · kickoff —	Repositories in scope —	CI/CD platform —
[START DATE] · week 1 —	Fallback squad —	Observability backend —
[ENGAGEMENT ID] —	Review latency baseline —	Event bus / messaging —
Binding assessment frameworks —	Rework rate baseline —	Compute platform —
Change freezes in window —	Change lead time baseline —	Service catalog / CMDB —
Executive sponsor —	[\$X] incremental run cost ceiling —	Data class out of bounds —
	Which value drivers we report —	Seven named roles · slide 14 —
Where this arrives filled in before the session, the kickoff runs thirty minutes shorter and slide 7 becomes a review rather than a live exercise. That is the single highest-leverage piece of preparation available.		
